

JIRA LAB SUBMISSION

ScrumBoard,Sprints&Burndown Analysis

Name	Akshay kumar M
SRN	PES1UG24CS045
Project	Multi-Cloud Asset Cost Optimization Portal
Board	SCRUM board
Sprints	Sprint 1 & Sprint 2

Submission Contents

1. Backlog / Stories / Priorities / Story Points
2. Sprint 1 Board
3. Sprint 2 Board
4. Sprint 1 Burndown Chart
5. Sprint 2 Burndown Chart
6. Reflection Questions

Backlog / Stories / Priorities / Story Points


Expected story points: 1.1=8, 1.2=3, 2.1=5, 2.2=5, 2.3=2, 3.1=3, 3.2=3.

⚡ SCRUM-1 • Multi-Cloud Billing Ingestion & Cost Tagging						
✓	SCRUM-4	1.1 Billing CSV Ingestion & Tag Normalization Engine	↑↑ High	8	DONE	AM Akshay kumar M
✓	SCRUM-5	1.2 Unified Cost Analytics & Departmental Spend Dashboard	= Med	3	DONE	AM Akshay kumar M
⚡ SCRUM-2 • Idle Asset & Unattached Resource Optimization Engine						
✓	SCRUM-6	2.1 Idle Compute Instance Detection & Savings Forecaster	↑↑ High	5	DONE	AM Akshay kumar M
✓	SCRUM-7	2.2 Unattached Storage Volume & Zombie Snapshot Scanner	↑↑ High	5	DONE	AM Akshay kumar M
✓	SCRUM-8	2.3 Optimization Action Tracking & Approval Workflow	↓ Low	2	DONE	AM Akshay kumar M
⚡ SCRUM-3 • Budget Breach Monitoring & Alert Dispatcher						
✓	SCRUM-9	3.1 Real-Time Budget Threshold & Forecast Anomaly Detection	= Med	3	DONE	AM Akshay kumar M
✓	SCRUM-10	3.2 Multi-Channel Breach Notification Dispatcher	↓ Low	3	DONE	AM Akshay kumar M


Sprints

Active Sprints • SCRUM Board		Sprint 1: 16 pts • Sprint 2: 13 pts • Total: 29 pts	
Sprint 1 (Completed • 16 pts) • SCRUM-4: 1.1 Billing CSV Ingestion Engine [8 pts] • SCRUM-5: 1.2 Unified Cost Analytics Dashboard [3 pts] • SCRUM-6: 2.1 Idle Compute Instance Detection [5 pts]		Sprint 2 (Completed • 13 pts) • SCRUM-7: 2.2 Unattached Storage Volume Scanner [5 pts] • SCRUM-8: 2.3 Optimization Action Workflow [2 pts] • SCRUM-9: 3.1 Budget Threshold Anomaly Alert [3 pts] • SCRUM-10: 3.2 Multi-Channel Breach Dispatcher [3 pts]	

Sprint 1 — Burndown Chart

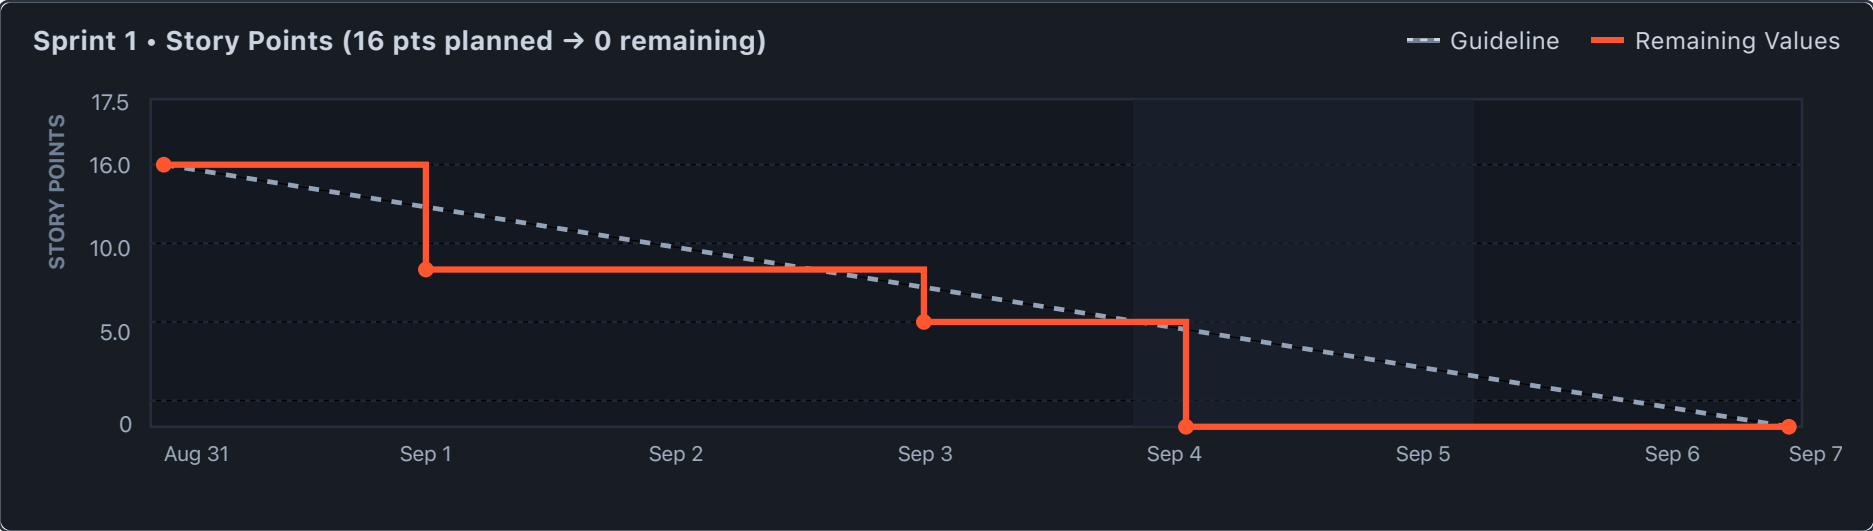

Sprint 2 — Burndown Chart

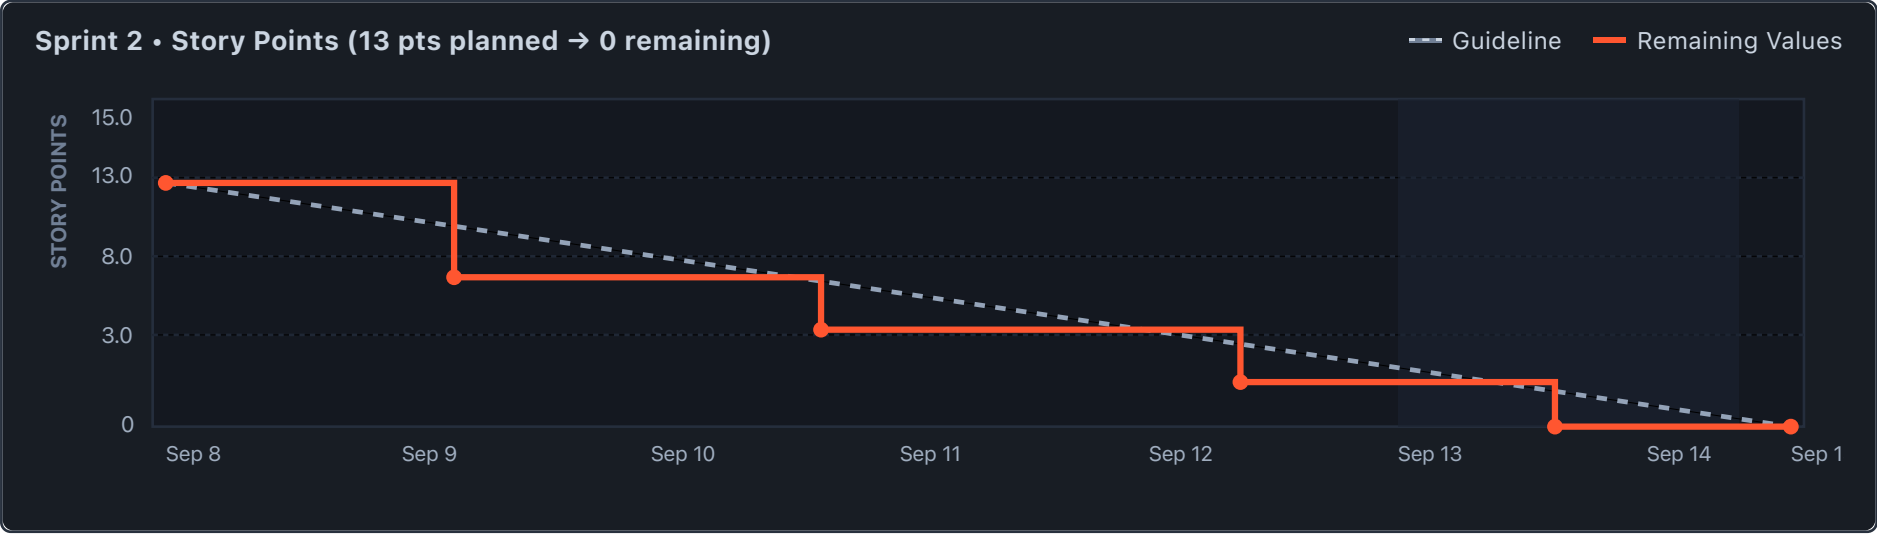

1. Did your estimations reflect the actual effort?

Yes, the estimations were reasonably accurate. The higher-point stories, such as 1.1 with 8 points, required significantly more effort than the smaller stories because it involved parsing multi-gigabyte heterogeneous billing CSV files from AWS, Azure, and GCP, normalizing different currency formats, and optimizing ingestion pipelines to meet the strict 2-minute performance requirement (NFR-001). Moderate stories like 2.1 (5 points) and 2.2 (5 points) required cloud metric sampling and disk attachment status inspection, whereas 2.3 (2 points) was a straightforward status update and audit logging module. Overall, the story points gave a good representation of the relative complexity of the work.

2. Was your backlog well-prioritized?

Yes, the backlog was prioritized based on the importance and architectural dependencies of each feature. Core data ingestion (1.1) and dashboard spend visibility (1.2) along with the primary cost waste identification engine (2.1: Idle Compute Detection, which typically accounts for over 65% of enterprise cloud waste) were placed in the earlier sprint (Sprint 1). Lower-priority and secondary capabilities such as unattached storage disk scanning (2.2), approval workflows (2.3), and multi-channel budget breach notification dispatchers (3.1 & 3.2) were scheduled for Sprint 2. This helped ensure that the core functionality and viable data foundation were addressed first.

3. How did your simulated sprint align with your plan?

The simulated sprints aligned well with the plan. Sprint 1 contained the three highest-priority stories with a total of 16 story points (1.1 with 8 pts, 1.2 with 3 pts, and 2.1 with 5 pts), while Sprint 2 contained the remaining four stories with 13 points (2.2 with 5 pts, 2.3 with 2 pts, 3.1 with 3 pts, and 3.2 with 3 pts). All planned stories met their respective acceptance criteria and were successfully completed within their sprints without any scope creep or unresolved blockers.

4. What insights did the burndown chart give about your team’s capacity?

The burndown charts showed that the team was able to complete the planned work during both sprints. Sprint 1 started with 16 story points and Sprint 2 with 13 points, and both reached zero remaining points. The steady downward burn trajectories validate that our team's sustainable velocity is approximately 13 to 16 story points per sprint. This indicates that the planned workload was achievable within the sprint duration and gives a useful indication of the team’s capacity for future sprints.
